

# SDCC Network Operations Status Report (Feb 18, 2021)

---

Alexandr ZAYTSEV


[alezayt@bnl.gov](mailto:alezayt@bnl.gov)

## Project: SDCC Network Operations & Interventions

### Chart

This chart shows the number of issues **created** vs. the number of issues **resolved** in the last **1260** days.

Previous Report

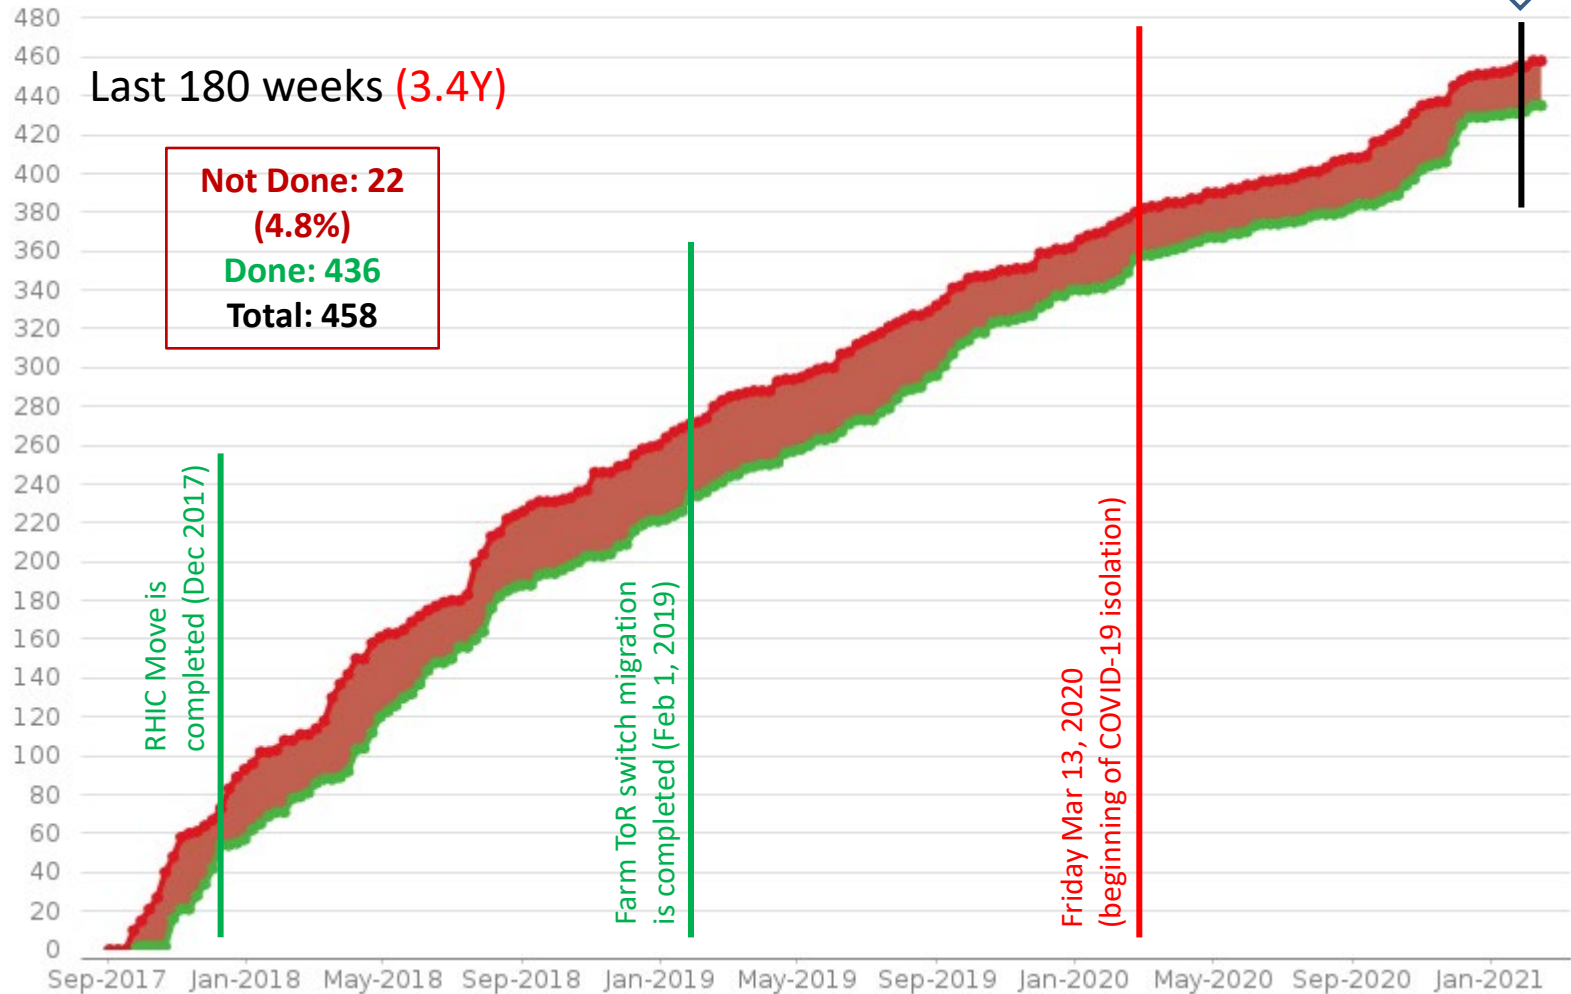


## Project: SDCC Datacenter B515/B725 Transition (CY20-23)

### Chart

This chart shows the number of issues **created** vs. the number of issues **resolved** in the last **1260** days.

Previous Report

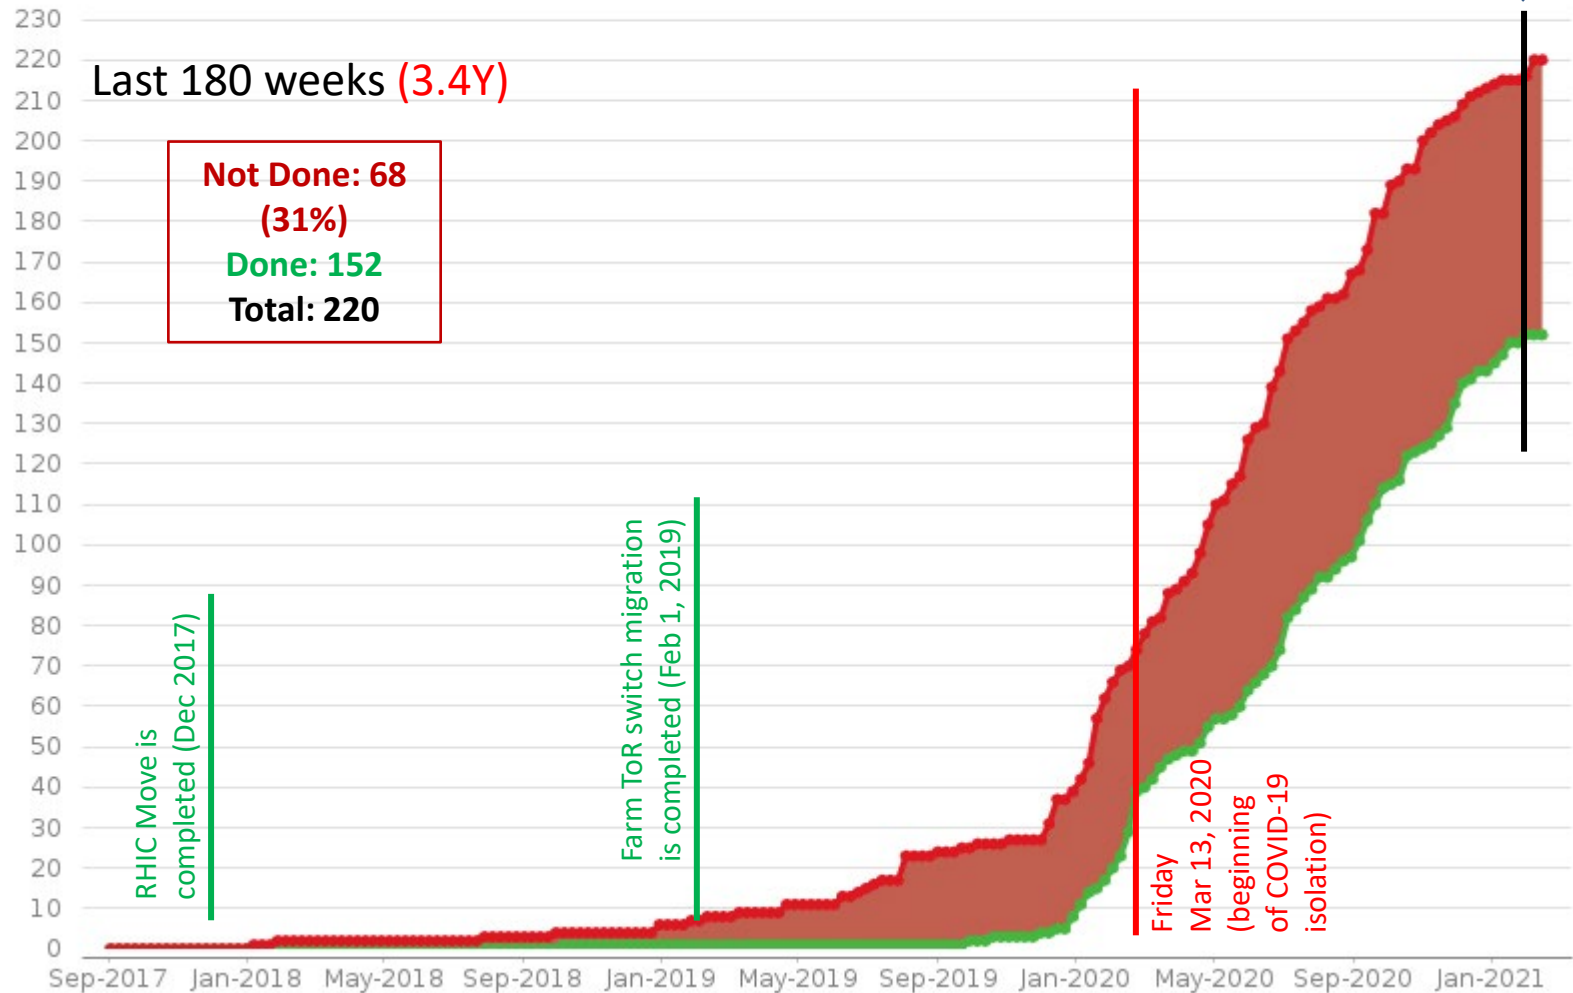

# Ongoing/Upcoming Interventions and Equipment Deployment/Retirement Operations

- NSLS II interbuilding link to SDCC Data center is expected to be upgraded from 4x 40 GbE to 4x 100 GbE later this month (Feb'21) – [pending equipment delivery](#)
- Replacement switches for s752/s753 switch pair in row 41S in B515/CDCE (serving HPSS subnet .11 to CDCE and BCF) are [ready for migration of clients to them at any convenient moment before the end of FY21](#)
- Pre-deployment of all fiber and copper materials purchased for B725 datacenter and currently placed in B515/main BCF to B725/area 1-171 – [pending the completion of configuration of the destination area for receiving these materials](#)
- Composition of the infrastructure racks of PS #2 area of the B725 MDH [is being finalized](#)
- Mechanical deployment of the rack frames in PS #2 area of the B725 MDH may commence in Mar-Apr 2021 already – [pending confirmation from the CFR project on the timeframe](#)

# Questions & Comments
