


SDCC Network Operations Status Report (Jan 20, 2022)

Alexandr ZAYTSEV
alezayt@bnl.gov

NETOPS Update – Jan 20, 2022

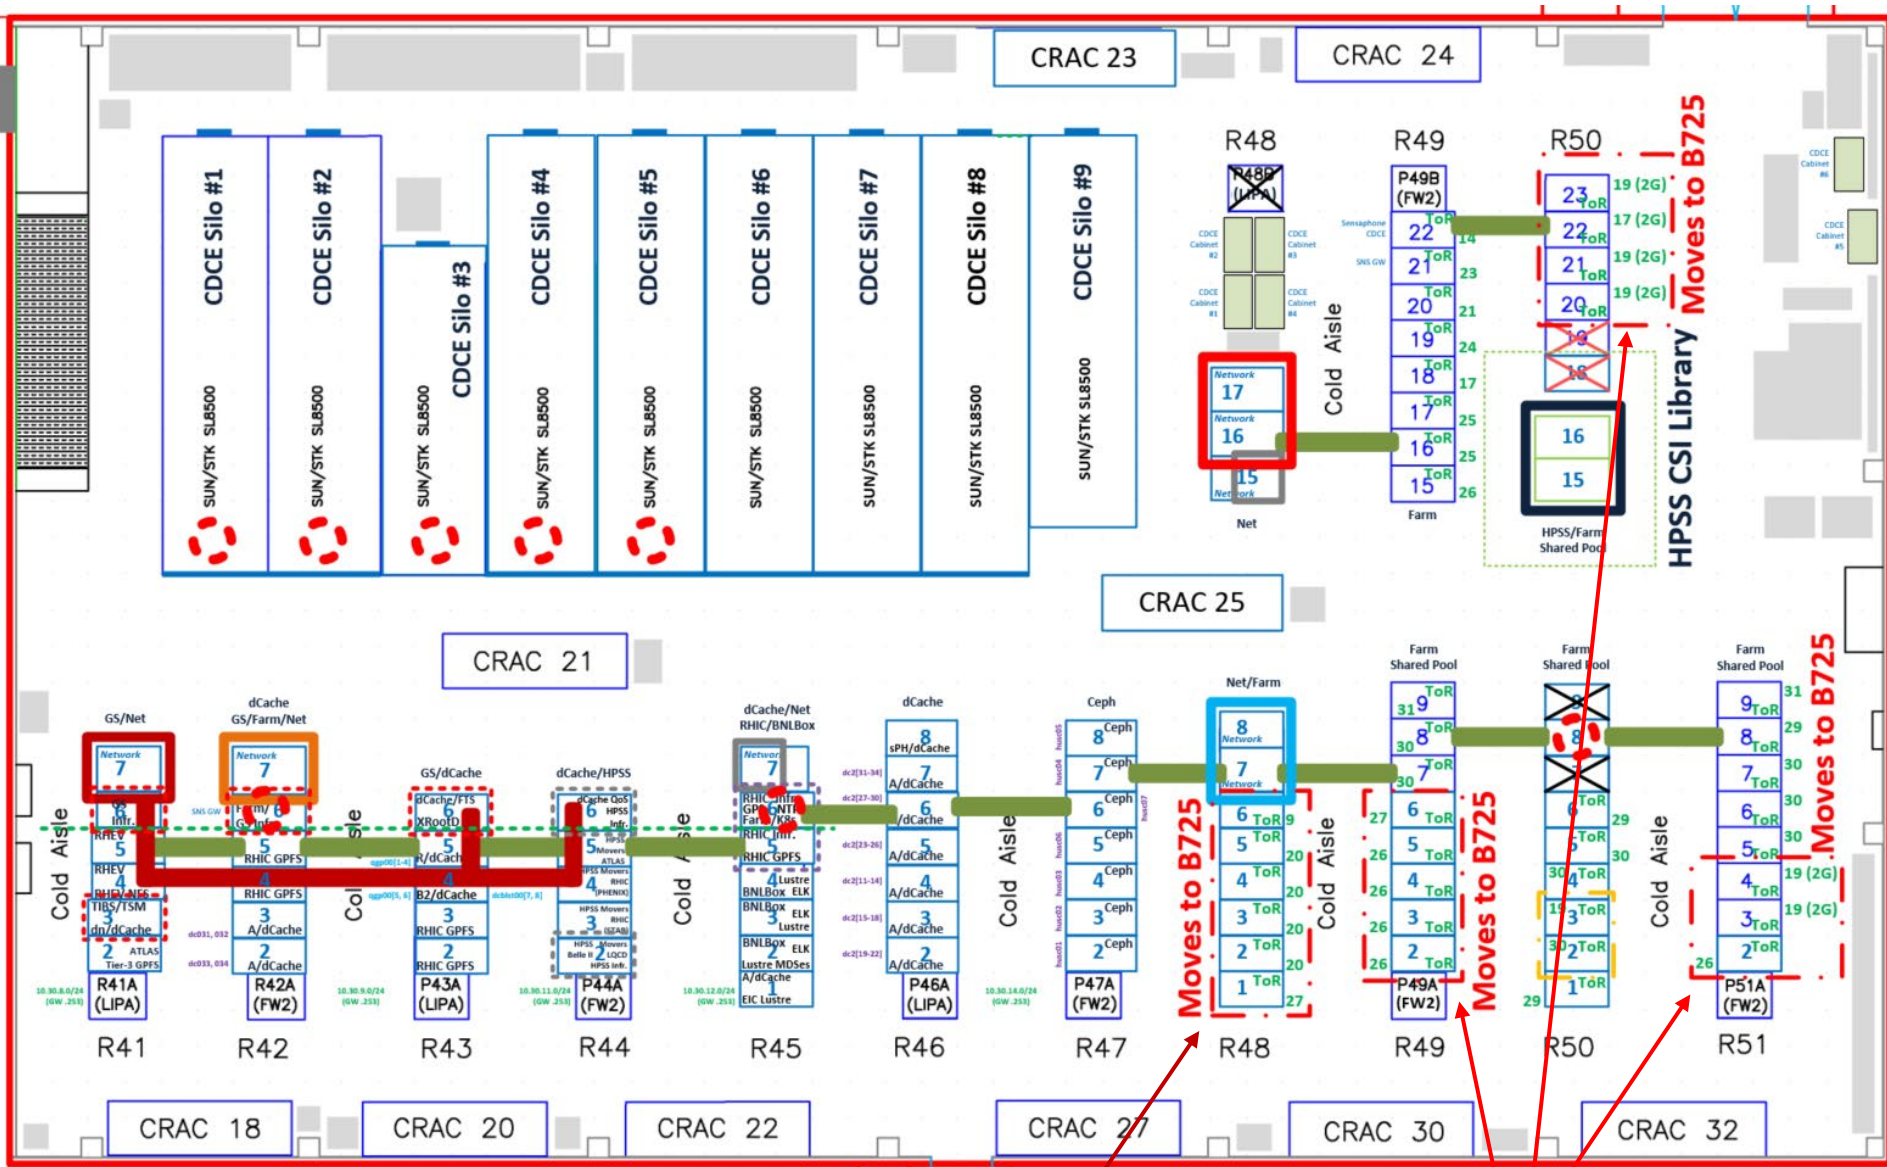

Jan 20, 2022

6x CPU racks moved to B725/MDH in 2021Q4


12x CPU racks moved to B725/MDH in Jan 2022

22x older CPU racks remaining
on the floor of CDCE to be
retired in place over time




18x CPU racks migrated from B515/CDCE to B725/MDH

(as of Jan 7, 2022)

A photograph showing the rear of a long row of black server racks in a data center. Blue indicator lights are visible on the back of the racks. The racks are densely packed with components, and various cables are visible at the top.

Back of the first
completed 20-rack
CPU row 107 (AE)

A photograph showing the front of a long row of black server racks. The racks have mesh doors. Some racks have "SUPERMICR" and "APC" logos. Green status lights are visible on the right side of the racks. A complex network of blue and black cables is visible above the racks.

Front of the
first completed
20-rack CPU row
107 (AE)

5x additional new CPU racks deployed in row 105 (V):


2 racks are 10G connected, 3 are still waiting for the ToR switches from late FY21 purchase to be shipped (expected in Feb'22)



NETOPS Update – Jan 20, 2022

B725 Tape Room

IBM TS4500 Library Complex

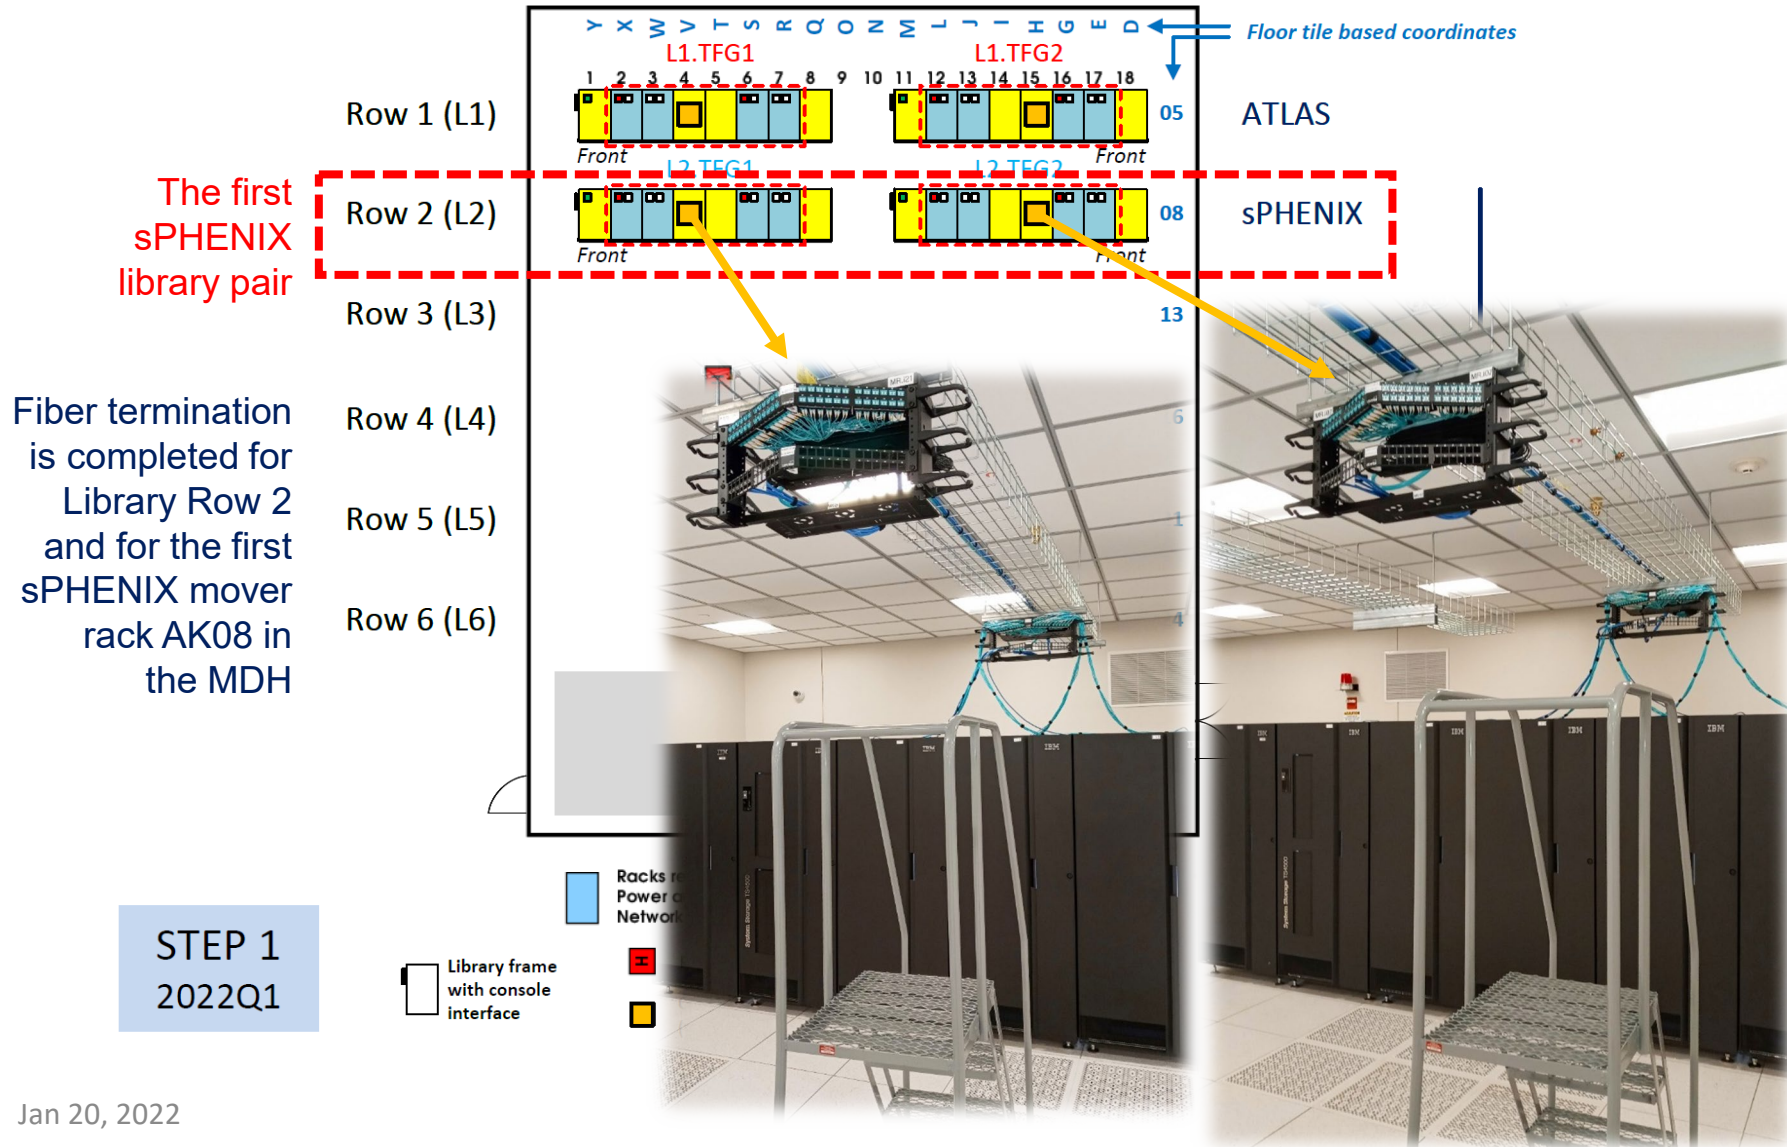

Questions & Comments
