
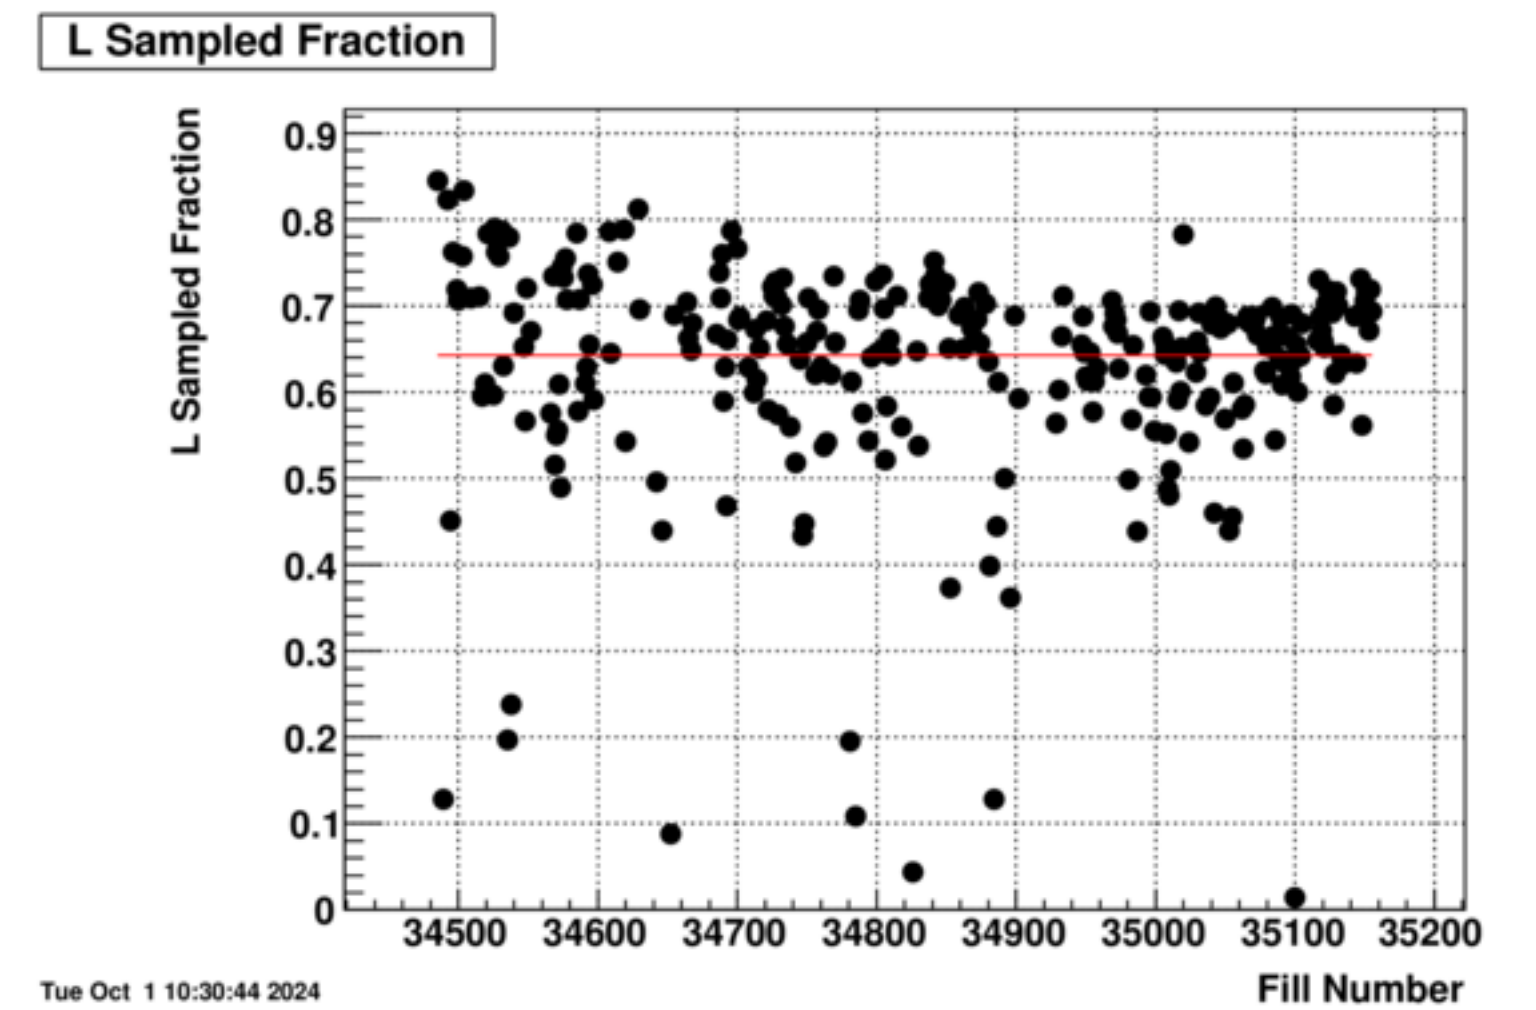
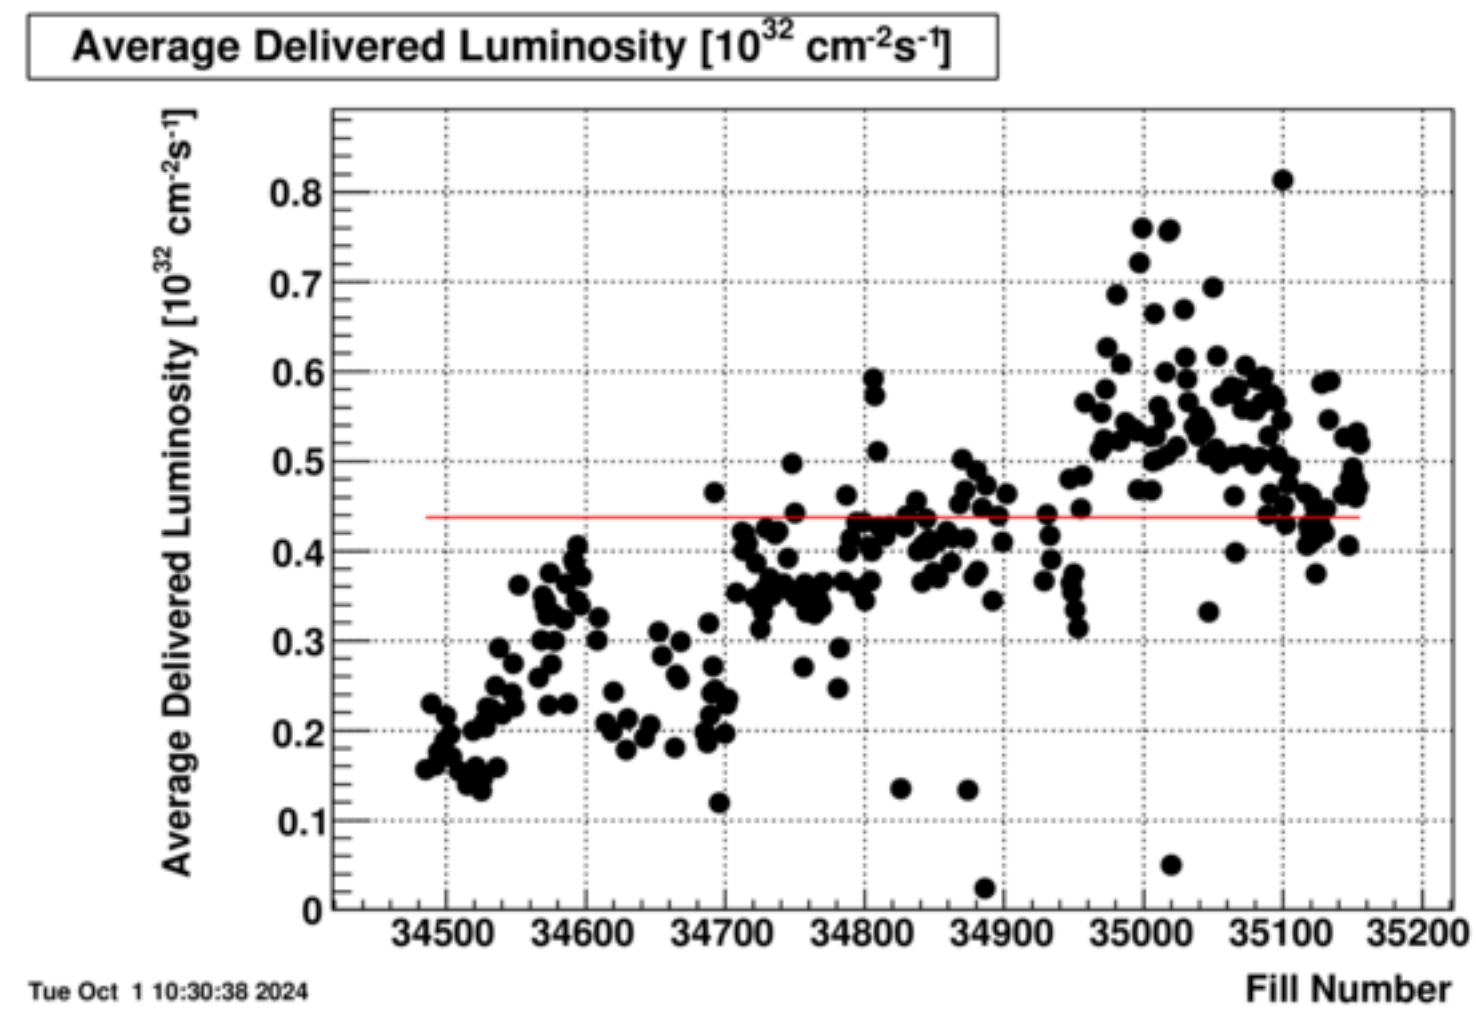
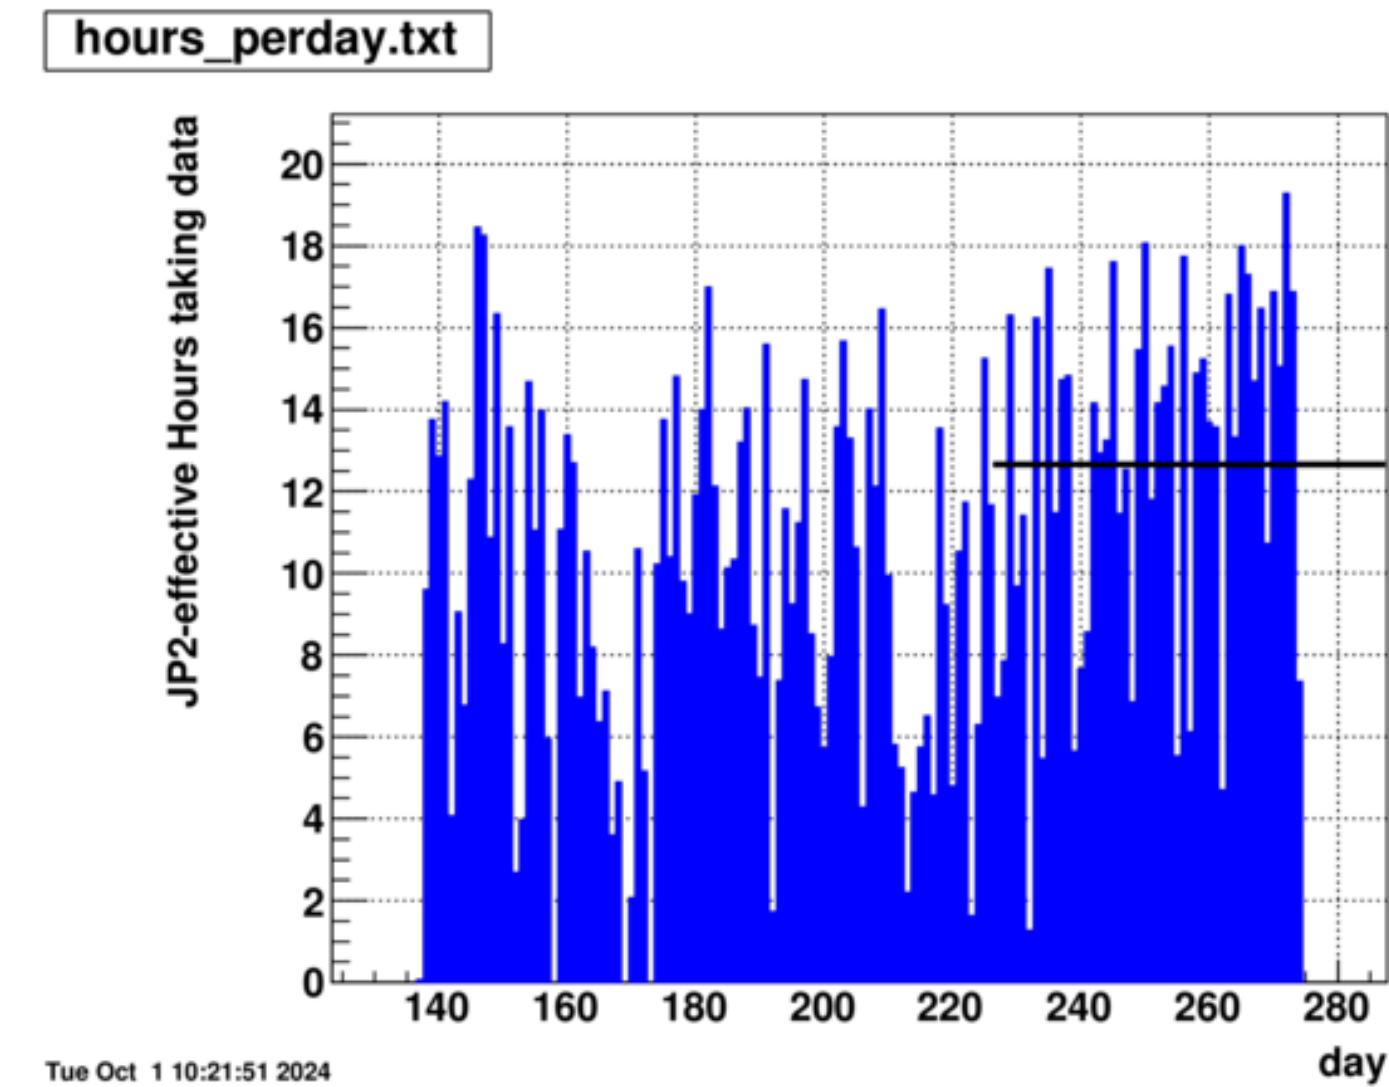
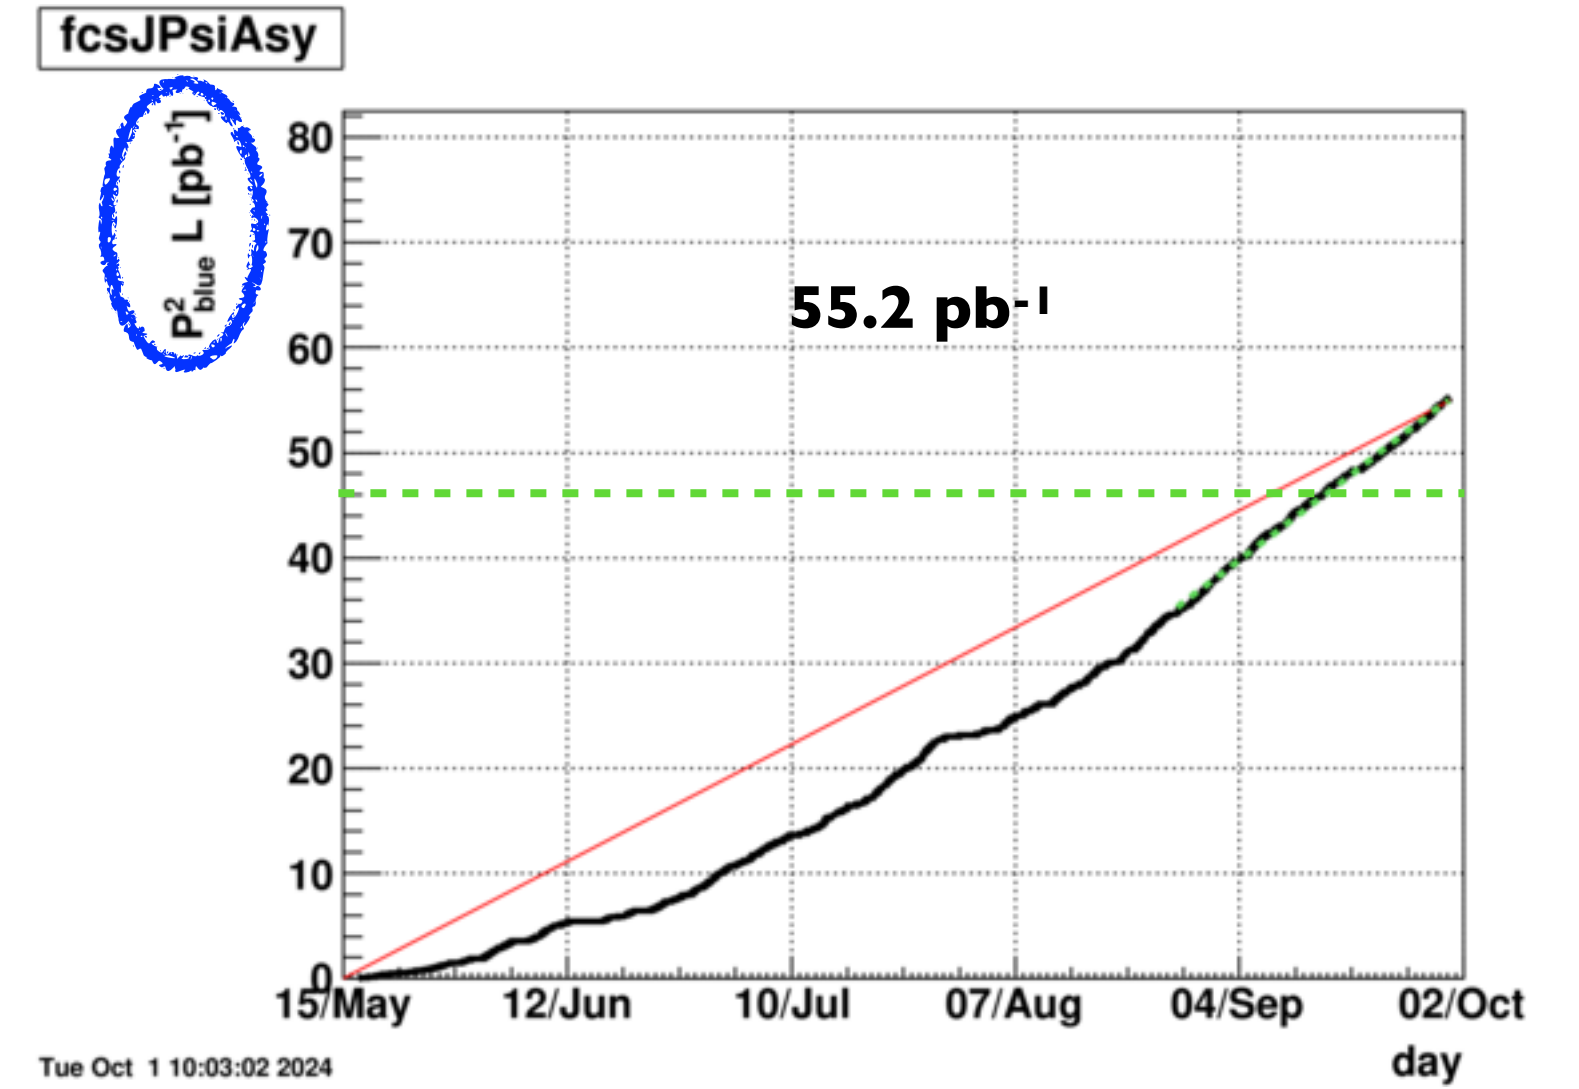
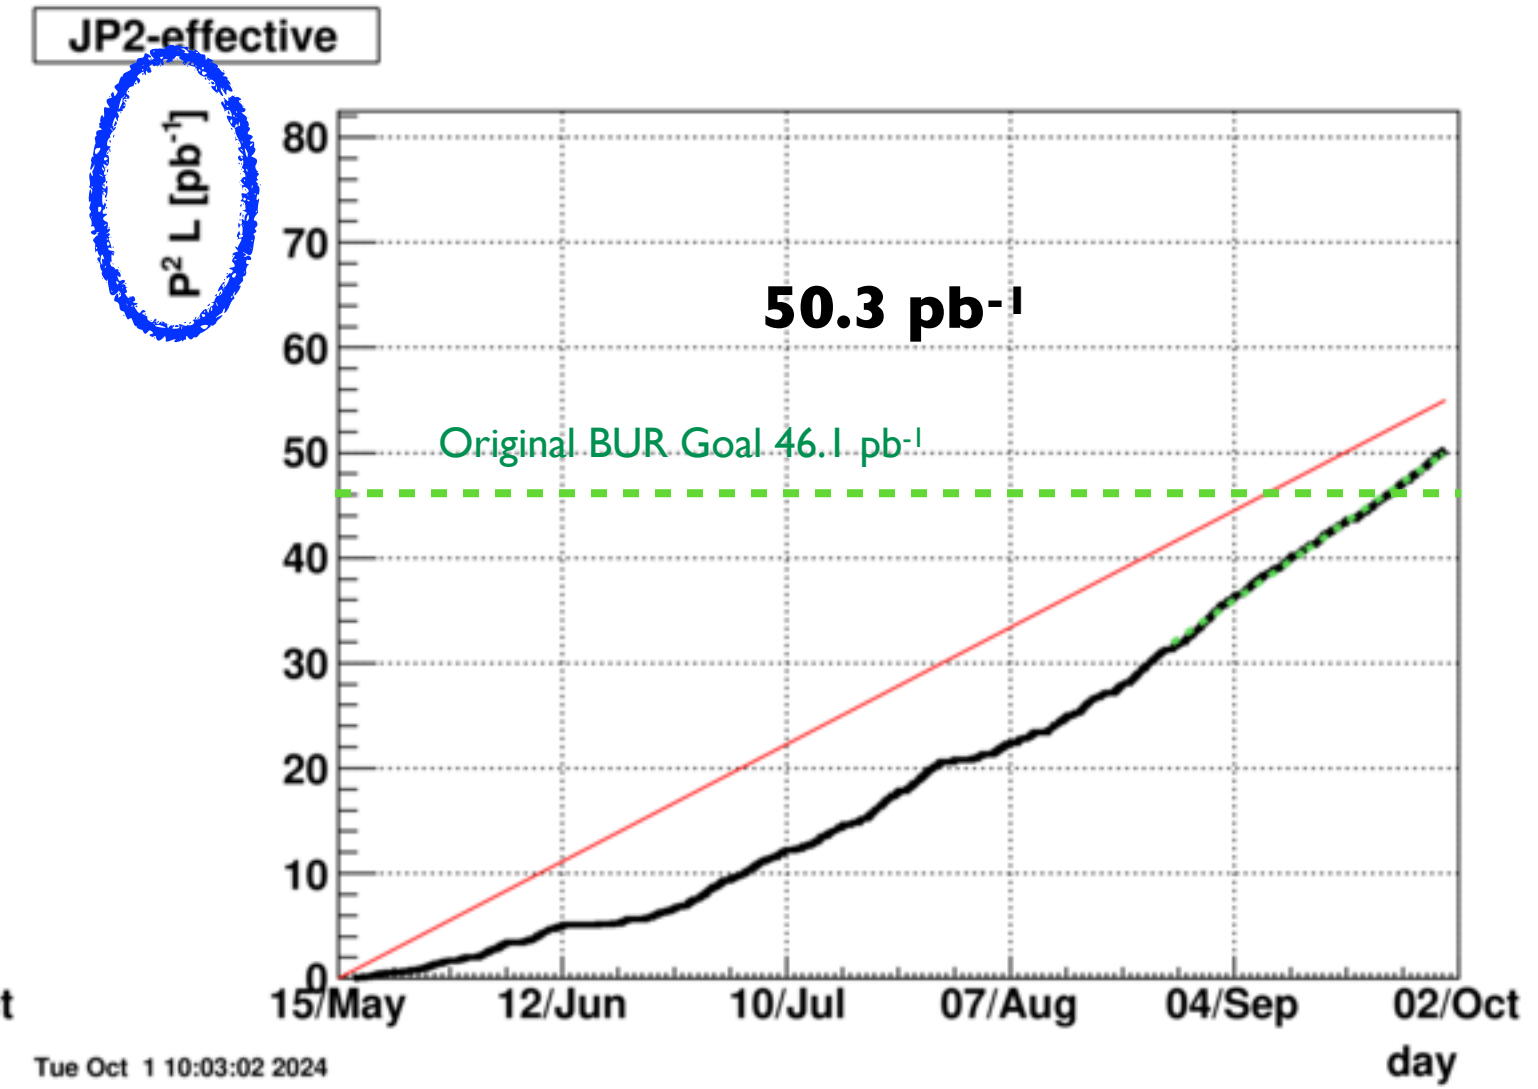


Run24 pp high luminosity (May 17 - Sep 30)

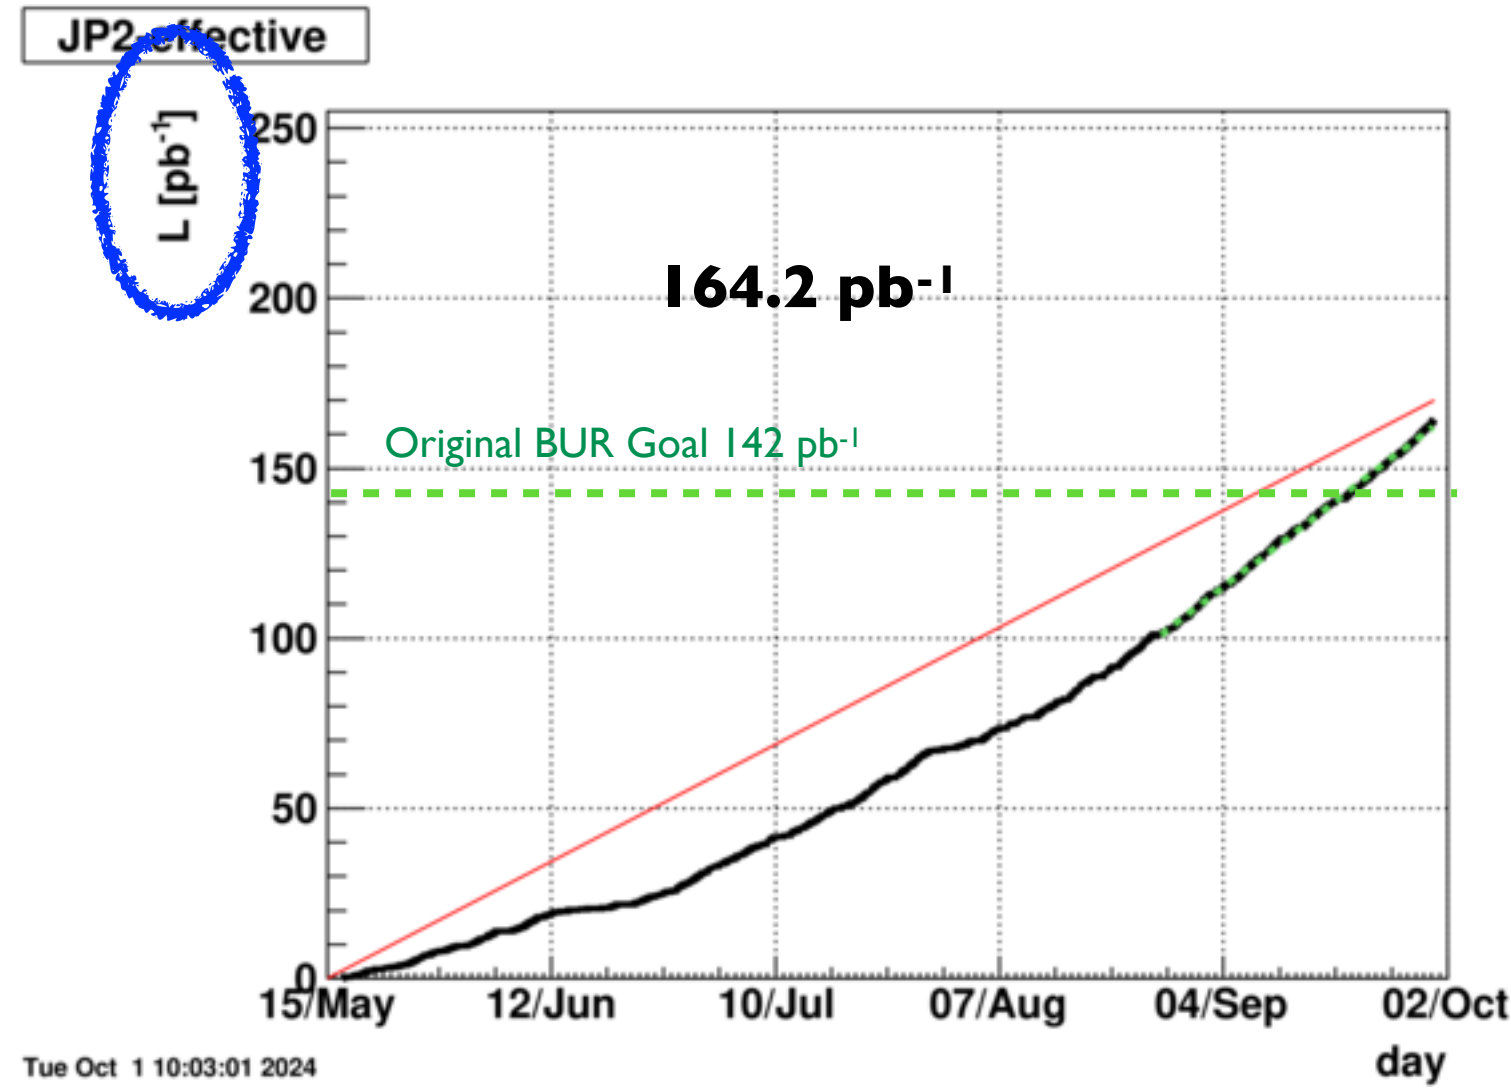

Shutdown schedule (preliminary)

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	2014	2024	2034	2044
1		Shutdown START	0 days	Mon 10/21/24	Mon 10/21/24				10/21		
2		Shutdown Prepration	7 days	Mon 10/21/24	Tue 10/29/24						
3		Remove Ground Strap	1 day	Mon 10/21/24	Mon 10/21/24	1	STSG		STSG		
4		Remove BBC and EPD	3 days	Mon 10/21/24	Wed 10/23/24	1	STSG,M Techs[200%]		STSG,M Techs[200%]		
5		Blowout Coils	1 day	Thu 10/24/24	Thu 10/24/24	4	STSG		STSG		
6		Remove East Poletip	1 day	Fri 10/25/24	Fri 10/25/24	5	STSG,M Techs		STSG,M Techs		
7		Remove West Poletip	1 day	Mon 10/28/24	Mon 10/28/24	6	M Techs,STGC		M Techs,STGC		
8		Install E Scaffold	1 day	Tue 10/29/24	Tue 10/29/24	7	Carpenters		Carpenters		
9		Install West Scaffolding	1 day	Tue 10/29/24	Tue 10/29/24	7	Carpenters		Carpenters		
10		TPC /iTPC Maintenance START	0 days	Tue 10/29/24	Tue 10/29/24	9			10/29		
11		TPC/ iTPC Maintenance END	0 days	Mon 1/27/25	Mon 1/27/25	18			1/27		
12		Final Tasks	27 days	Mon 1/6/25	Tue 2/11/25						
13		Global Interlock Testing	5 days	Mon 1/6/25	Fri 1/10/25		M Techs[200%]		M Techs[200%]		
14		Remove West Scaffolding	1 day	Mon 1/13/25	Mon 1/13/25	13	Carpenters		Carpenters		
15		Install West Poletip	1 day	Tue 1/14/25	Tue 1/14/25	14	M Techs,STSG		M Techs,STSG		
16		EEMC Maintenance	7 days	Wed 1/15/25	Thu 1/23/25	15	M Techs[200%]		M Techs[200%]		
17		Remove East Scaffolding	1 day	Fri 1/24/25	Fri 1/24/25	16	Carpenters		Carpenters		
18		Install East Poletip	1 day	Mon 1/27/25	Mon 1/27/25	17	M Techs[200%]		M Techs[200%]		
19		Fill Magnet with Water (Low Flow)	2 days	Tue 1/28/25	Wed 1/29/25	18	STSG,Water Grp		STSG,Water Grp		
20		Start Magnet Water (High Flow)	1 day	Thu 1/30/25	Thu 1/30/25	19	STSG,Water Grp		STSG,Water Grp		
21		Magnet Power Supply Testing and Heat Run	5 days	Fri 1/31/25	Thu 2/6/25	20	Pablo		Pablo		
22		TPC HV Test	1 day	Fri 2/7/25	Fri 2/7/25	21	Alexi		Alexi		
23		Start flow of Flammable Gases	1 day	Mon 2/10/25	Mon 2/10/25	22					
24		Install EPD and Small BBC Tiles	2 days	Mon 2/10/25	Tue 2/11/25	22	EPD Group,STSG		EPD Group,STSG		
25		Commisioning with Cosmic Rays	7 days	Tue 2/11/25	Wed 2/19/25	23					
