

Status







Booster Running for setup and NSRL

Switch G09C Ready, H11 testing into dummy

AGS

G10: Ready

No access planned for this week

RHIC:



COOLING DOWN...



PROGRESS UPDATED IN REAL TIME HERE

Other RHIC items:


Emergency generator tests for May completed

Adjacent areas
(Berms etc.) will be locked this week

ORC items items rechecked prior to setup with beam

Sector 2 and 4Z1
RF testing as
necessary

RHIC Ring sweeps Friday, exps Saturday morning Access cartoon from "This_Week (https://www.agsrhichome. bnl.gov/AGS/Accel/Mainten ance/Schedules/This_week. htm#daily)

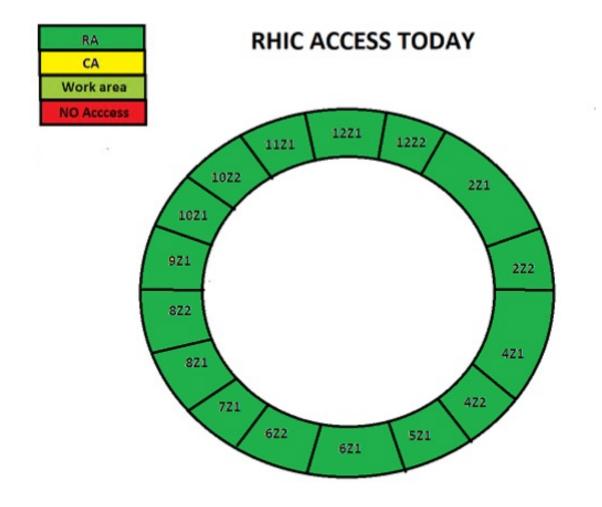

Prepared by: P. Sampson		Tue, 5/20/2025														
27-May		1	Days/column:	1		May 23, 2025	May 31, 2025	Jun 4, 2025		Jun 8, 2025		Jun 12, 2025		Jun 16, 2025		Jun 20, 20
TASK	PROGRESS	START	END				S S M T								19 20 T F	21 22 5 S
Remove Electrical LOTO	100%	5/1/25	5/1/25	0												
Install vacuum belows, pump down	100%	5/5/25	5/7/25	2												
install BPM cables	100%	5/7/25	5/7/25	0												
Weld RUSH LINES	100%	5/7/25	5/7/25	0												
Remove cryo LOTO for RUSH pressure/leak tests	100%	5/7/25	5/7/25	0												
Inspect, sniff RUSH lines	100%	5/7/25	5/7/25	0												
Install cryo sensors	100%	5/7/25	5/7/25	0												
Weld shells closed, inspect	100%	5/6/25	5/10/25	4												
Begin pump and purge	100%	5/7/25	5/7/25	0												
PUMP AND LEAK TEST	100%	5/10/25	5/14/25	4												
Leakcheck vacuum vessel	100%	5/14/25	5/14/25	0												
Pump down insulating vacuum	100%	5/14/25	5/16/25	2												
Restore and test VOHD	100%	5/16/25	5/16/25	0												
45kCOOL DOWN	95%	5/15/25	5/27/25	13												
4k cooldown	0%	5/28/25	5/31/25	3												
Install BLMs Rempve LOTO	100%	5/26/25	5/26/25	0												
Sweep berm areas	85%	5/27/25	5/27/25	0												
Sweep RHIC Tunnel	0%	5/30/25	5/31/25	1												
Hi- Pot at 4k and resume setup	0%	5/31/25	5/31/25	0												
