
RACF/SDCC Network Operations Status Report (May 2, 2019)


Alexandr ZAYTSEV

alezayt@bnl.gov

Project: Post RHIC Migration BCF & CDCE Cleansing & Service Normalization (2018Q1-2019Q2)

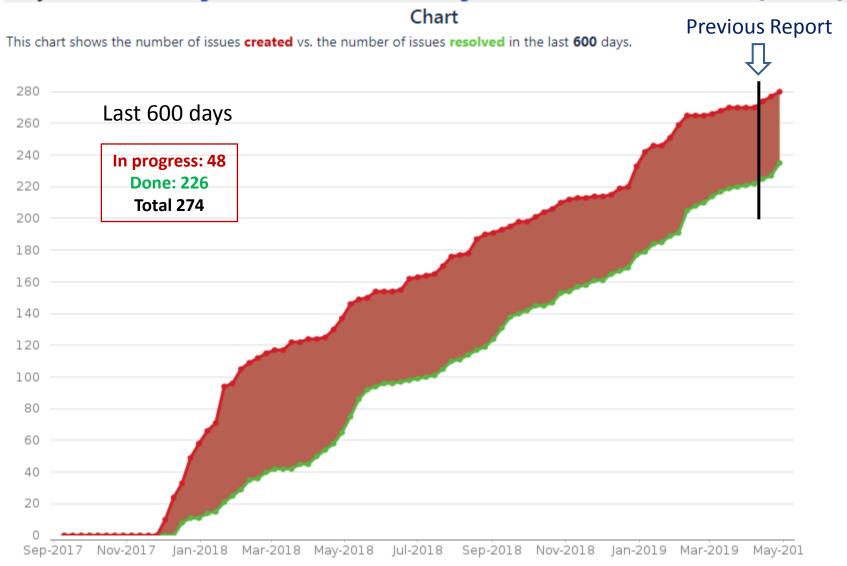

Project: RACF/SDCC Network Operations & Interventions

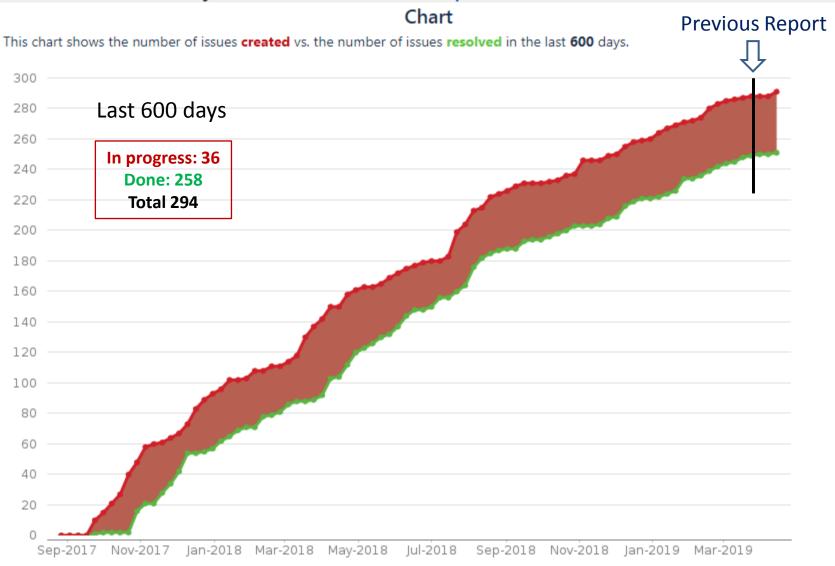


Ongoing/Upcoming Interventions and Equipment Deployment/Retirement Operations (1)

- New ATLAS Tier-1 storage installation in CDCE (6 racks, 21.6 PB usable in the final config)
 - 24 out of 24 disk arrays are received, 25 out of 25 storage servers are received
 - 3 new storage racks out of 6 are being placed in production
 - The data migration to the 3 out of 6 new racks of ATLAS dCache storage is complete
 - All racks of new ATLAS Tier-1 dCache purchase are now powered up at their final location and provided with network uplinks
 - Second half of the data copy process is yet to start
- Preparations for the purchase of the first rack of new RHIC HPSS movers (rack 44-4) and the
 OSD nodes for the new ATLAS Ceph cluster is entering the final stages IN PROGRESS
- Preparations for the B515 SciCore replacement:
 - The replacement of **phnxwrt** host group is being prepared for deployment in rack 45-6 (to be migrated out of the s770/s771 switch pair to the Storage Core) – DONE
 - Former HPC home directories GPFS and CFN GPFS are being moved out the s770/s771 switch pair to the Storage Core tomorrow (Apr 5, 2019) – DONE
 - Row 17 and 16 cleanup is in progress


Ongoing/Upcoming Interventions and Equipment Deployment/Retirement Operations (2)

- LQCD dCache installation (rack 44-6)
 - A single repurposed serve is provided with network uplinks, another one will join later
- Rack position 45-5 to be freed by moving the existing Hitachi H130 rack to Sigma-7 next week
 - Potential place for the 2nd RHIC infrastructure rack replacing the rack 4-10 (right next to the 1st one in position 45-6 which is getting 75% full)
- Upcoming test HPSS libraries removal from the Facility (May 2019)
 - Single frame IBM TS5400 in row 15 DONE
 - 6 frame SpectraLogic T-Finity installation in row 3 Power down expected on May 20, 2019
- Retirement of the legacy CFN Gen.3
 - Rack 30-[4, 5] in the QCDOC
- ATLAS HPSS movers retirement.
 - Expected in row 17 shortly after this functionality is moved to the new equipment in row 44S in CDCE
 - Old ATLAS movers are being decommissioned DONE, HW retirement will follow as part of round 6
- Electrical work will continue in QCDOC area
 - Legacy CFN Gen.4 and CSC KBASE racks 30-[7-10] are affected DONE
 - Electrical work in QCDOC is finished (ready for new SF equipment)
 - Cleaning of the unused materials / floor tiles / cable bridges is in progress

Hardware Removal / Deployment Operations (1)

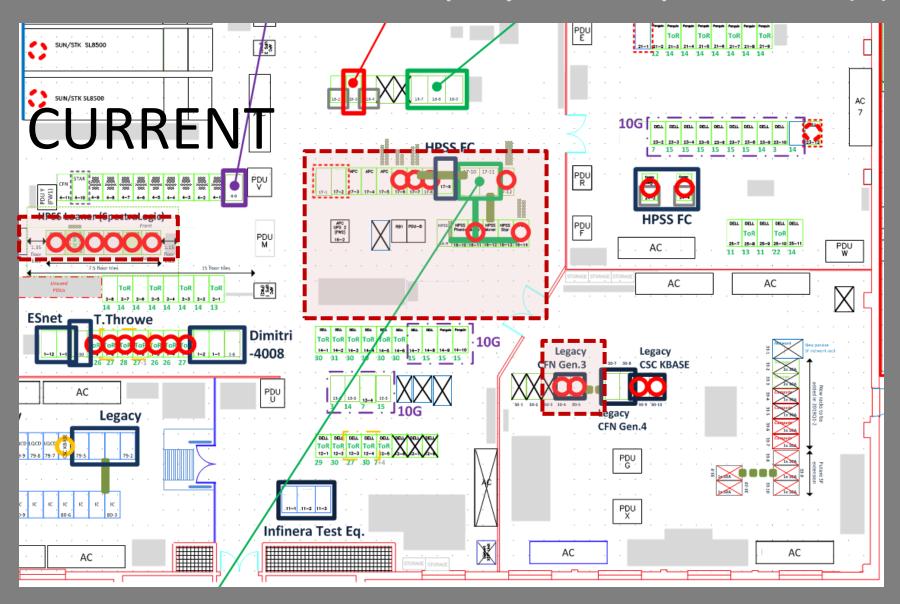

Hardware Removal / Deployment Operations (2)

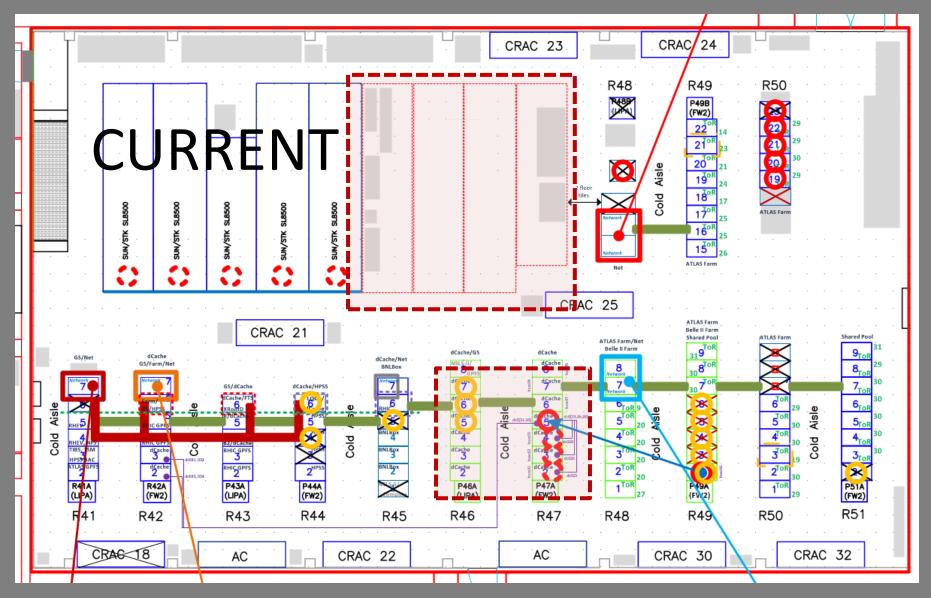

Hardware Removal / Deployment Operations (3)



Questions & Comments
