


Modules for 2017 prototype

Anne for the NPL
October 18, 2016

meshes arrived

- blocks 19 & 20 have complete sets
- first set already filled
- fibers: still no ship date that I know, pinged Kuraray again, but Sean C. is out this week

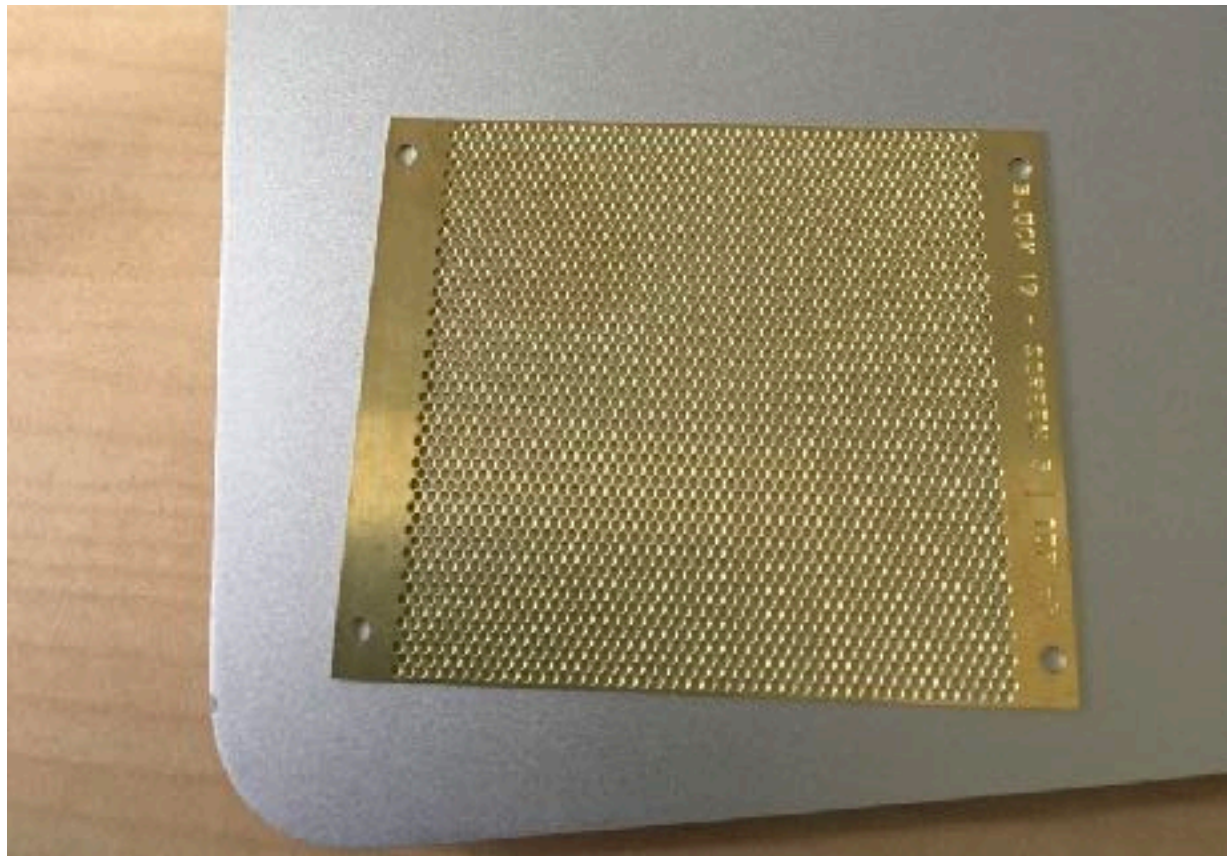

last generic block

- filled on Friday
- small patch job required otherwise looked good
- epoxy filling done very slowly (40 minutes)
 - building a manifold to do up to 4 blocks in parallel with a single pump
- will be machined and then sliced up to look at density variation / any voids

