News

- Incremental Design and Safety Review on ePIC PID detectors conducted on July 5-6: Review presentations; Final review report
- EIC Project Detector R&D Review on Aug 28/31: FY23 report and FY24 proposals; Review presentations; Close-out slides
- ePIC TOF Project Engineering Design
 - Mechanical engineering: support structure and cooling submitted on June 27: Mechanical PED
 - Electrical engineering: Low-jitter clock in DAQ, TOF Service Hybrid in eRD109 FY24 approved
 - Module prototyping? FBK production?

• ePIC TOF DSC

- Working on schedule and cost, identify institutional responsibilities and L5/L6 contacts
- BTOF: Mathew Gignac/Satoshi Yano/Zhenyu Ye, FTOF: Mathieu Benoit/Wei Li, Common System: Andreas Jung/Zhangbu Xu

ePIC TOF Simulation

- Updated geometry database September 29: consistency check/update in DD4Hep to be done
- TOF in tracking Nicolas: evaluate the TOF impact on tracking using latest software <u>10/17</u>. Re-check FTOF material budget impact
- TOF PID reconstruction Oskar/Zhenyu: reconstruction, validation plots
- TOF digitization Zhenyu: updated digitization parameters (see page 2); Adam/Souvik: charge sharing and detector noise
- TOF service in simulation TBD: implement the missing material for mechanical support structure, cooling and cabling

ePIC Collaboration meeting at ANL on January 9-13, 2024

- Parallel sessions on Jan 9-11 would include AC-LGAD, Electronics/DAQ, PID, tracking, ...
- AC-LGAD parallel session (Jan 9 full day + Jan 10 afternoon): https://forms.gle/LcLjyFq7ThfasYdJ9

11/21/23 Zhenyu Ye @ UIC

News

• Incremental Design and Safety Review on ePIC PID detectors conducted on July 5-6: Review presentations; Final review report

Detector

• (AC-LGAD) 35ps Barrel/ 25ps FW timing resolution seems to be almost the best performance without safety margin. Under these circumstances, a bias voltage scheme should be more flexible than only one pair of cables for each board, because the temperature gradient and the position-dependent radiation fluence require different operation voltages.

Thermal: Yi/AndyFluence: Wei/XiaoPower for Service

Hybrid: Tonko/Wei

- (AC-LGAD) The type of interconnection to the sensors (like wire bonding or bump bonding) must be clearly specified. If a detector uses a bump bonding connection, we would advise to start testing the flip-chipping process since it takes longer to develop a stable procedure.
- eRD109: ORNL
 - eRD112: UIC

- The initial requirements for the EICROC were specified mostly for the Roman Pot detector and not for all detectors which use EICROC. We advise summarizing the equirements for all detectors and making a single EICROC specification before submitting further prototype chips.
- A specification on the tolerable clock drift and the robustness to phase irregularities should be defined and will help to ensure that these parameters are measured and controlled in the architecture from the beginning of the design phase. The DAQ design should include a backup solution for a directly distributed clock to the RDO boards to provide the clock precision required by each subsystem.

 Zhenyu Ye @ UIC
- Tonko: 5ps jitter

Electronics

11/21/23

News

• Incremental Design and Safety Review on ePIC PID detectors conducted on July 5-6: Review presentations; Final review report

Tracking

- Recent progress has been made in ePIC's cross-cutting PID WG to understand tracking requirements for PID detectors. Requirements documents should capture the bi-directional interface between tracking and PID detectors: e.g., translation between extrapolated track impact point and angle resolution requirements for PID detectors. It could be evaluated where the PID subdetectors can contribute to improving the tracking performance and how in the reconstruction algorithms this could be integrated.
- Encouraging track momentum resolution improvement was achieved by including the AC-LGAD in reconstruction. The reviewers suggest extending this study to understand the impact on the extrapolated track impact point and angle at the radius of the DIRC.

Recommendations

1. Capture the bi-directional interface between tracking and PID detectors: e.g., translation between position and angular resolution requirements for PID detectors.


Schedule and Timeline

CD2/3 Review

- 10	2023	2024	2025	2026	2027	2028	2029	2030	2031	203
Project Milestones					 					
CD2/3										
IR6 ready for										
CD-4a									2.5	
CD4										
bTOF final design										
fTOF final design										
Sensor									T	
R&D										1313131313131313131
Pre-production										
Production										
QA										
ASIC										
R&D										
Pre-production										
Production										
QA										
Module Structure										
R&D										
Pre-production										
Production and QA										
Module Assembly										
R&D										
Pre-production							_			
Production										
QA										
Service										
R&D										
Production										
QA										
bTOF installation										
fTOF installation										
Software										
Sim. / Rec.										
Database										
Online										

Schedule and Timeline

Prelim Design (70%) Final Design Construction Completed Installation 11/2024 7/2026 7/2029 3/2030

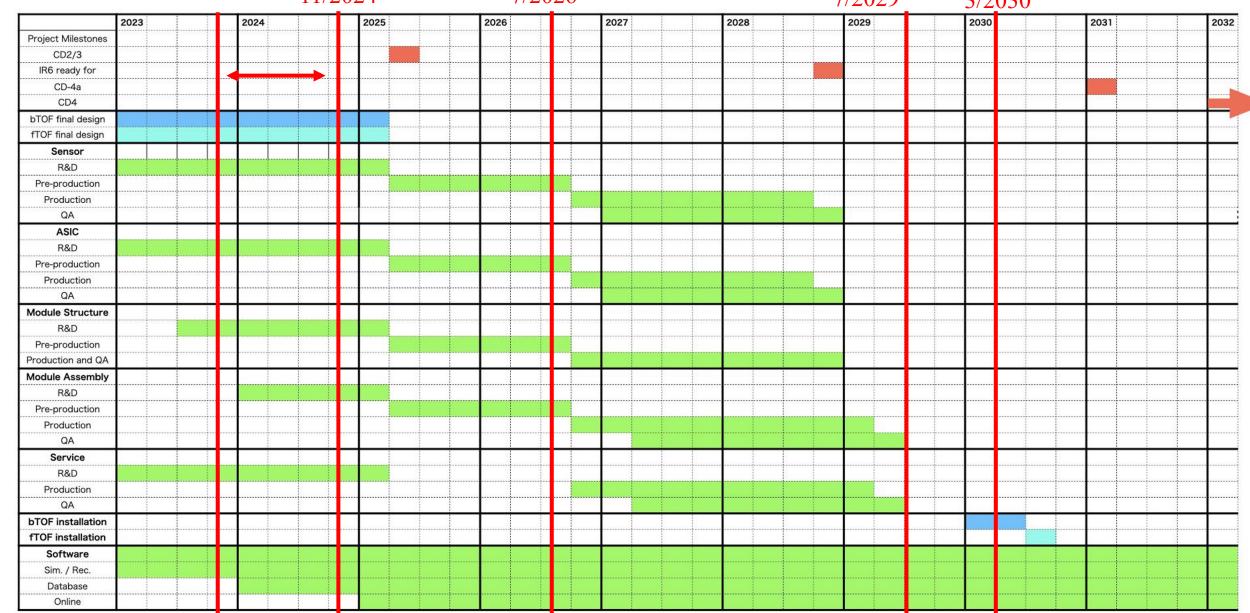

FY24 Plan

- Simulation
- R&D:
 - Sensor: new BNL+HPK production and Characterization, simulation, irradiation
 - Sensor-ASIC integration: interposer for BTOF, hybridization for FTOF pixel sensor-ASIC
 - ASIC: EICROC0/EICROC1, FCFDv1/v2
 - Module PCB: Low-mass flexible Kapton for BTOF
 - Module structure: Low-mass CF structure for BTOF module
 - Service Hybrid: RDO + Powerboard
- PED:
 - BTOF and FTOF $(5\%X_0)$ support structure
 - Module assembly: Mathew for BTOF next week?
 - FBK production: Mathew next week?
- TDR

AC-LGAD FY24 R&D Proposal

- Optimized sensor design and final prototypes that meet ePIC requirements, including timing and spatial resolution, irradiation tolerance, and reasonably large size for module assembly
- Prototypes of interposer for mechanical/electrical connections between strip sensor and ASIC
- Prototypes of light-weight module mechanical structures for forward TOF
- Prototypes of frontend ASICs
- Functional and full size low-mass Kapton PCB
- Low-cost interconnect for sensor-ASIC hybridization
- Service hybrid prototype

eRD112 (414k->286k\$)

- Sensor R&D (346k->261k\$)
 - BNL, HPK/FBK-productions
 - TCAD, lab/beam/irradiation tests
- Sensor/ASIC integration (15k\$)
 - Interposer
- Mechanical structure (\$53k)
 - Light-weight structure w. cooling

eRD109 (435k->390k\$)

- Frontend ASICs
 - EICROC (85k\$)
 - FCFD (40k\$)
 - 3rd Party ASICs (45k\$)
- Frontend electronics
 - Low-mass Kapton PCB (30k\$)
 - Low-cost sensor-ASIC hybrid. (15k)
 - Service hybrid (220k)

EPIC Simulation

- Geometry model, digitization and reconstruction
- Requirements on spatial, timing resolutions, and material budget


Project Engineering Design

- Engineering design for pre-TDR
- Integration & services

Sensor Electronics Sensor-ASIC integration Mechanics

8/28/2023 Zhenyu for eRD112

Proposed Working Package Structure

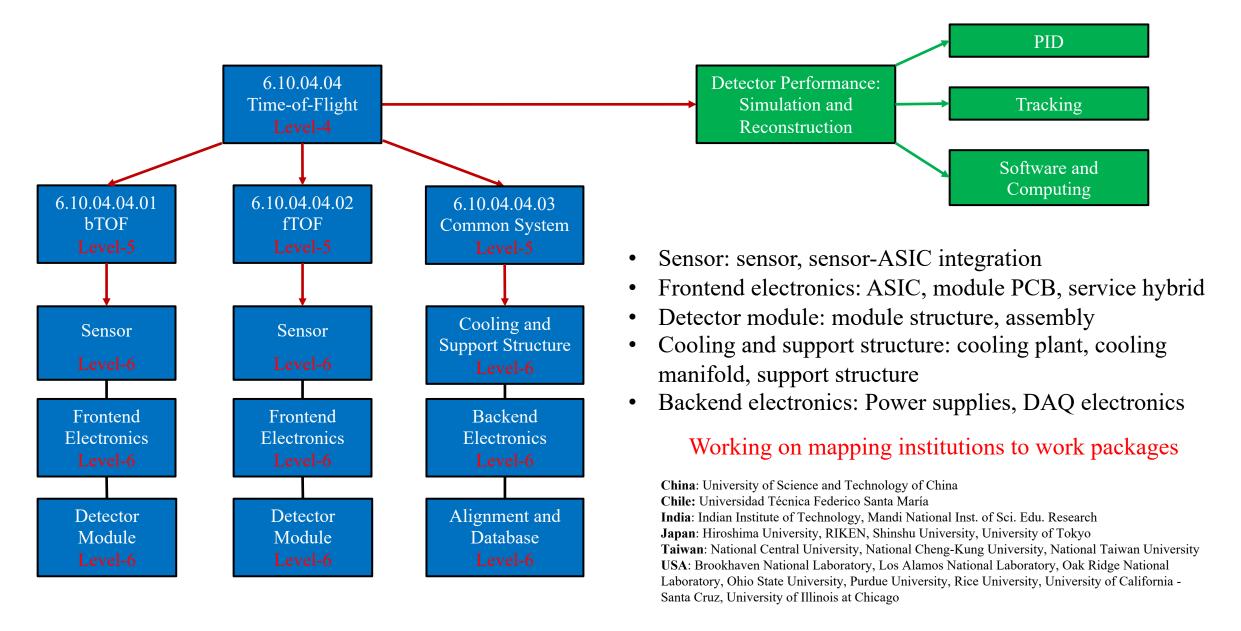

Barrel TOF

Package	Coordinator(s)	Institutions
Sensor		UCSC, Hiroshima+Shinshu, (BNL-HEP/IO, UIC/FNAL)
Sensor-ASIC integration		UCSC, (ORNL, Hiroshima, UIC)
Frontend ASIC		(IJCLab/Omega, FNAL), BNL, Hiroshima, (UIC)
Flex Module PCB		ORNL
Service Hybrid		BNL, (Rice, UIC)
Module Mechanical Structure		Purdue, NCKU
Module Assembly		UCSC, (BNL-HEP/IO, RIKEN)

Forward TOF

Package	Coordinator(s)	Institutions
Sensor		ORNL, SCNU
Sensor-ASIC integration		ORNL, (SCNU)
Frontend ASIC		(IJCLab/Omega), BNL, ORNL
Flex Module PCB		Rice, ORNL
Service Hybrid		Rice
Module Mechanical Structure		Purdue, NCKU
Module Assembly		LANL. ORNL. (RIKEN)

Common System

Package	Coordinator(s)	Institutions
Support Structure		Purdue, NCKU
Cooling System and Manifolds		
Patch Panel and Cables	Zhangbu Xu + Tim Camarda (BNL/KSU)	EIC project, KSU
LV Power Supplies	Zhangbu Xu + Tim Camarda (BNL/KSU)	EIC project, KSU
HV Power Supplies	Zhangbu Xu (BNL/KSU)	EIC project, KSU
Timing/DAQ System	Tonko Ljubicic (BNL)	EIC project, BNL
Alignment and Database		
