


STAR Status


RHIC Time meeting

September 2, 2025

Oleg Eyser

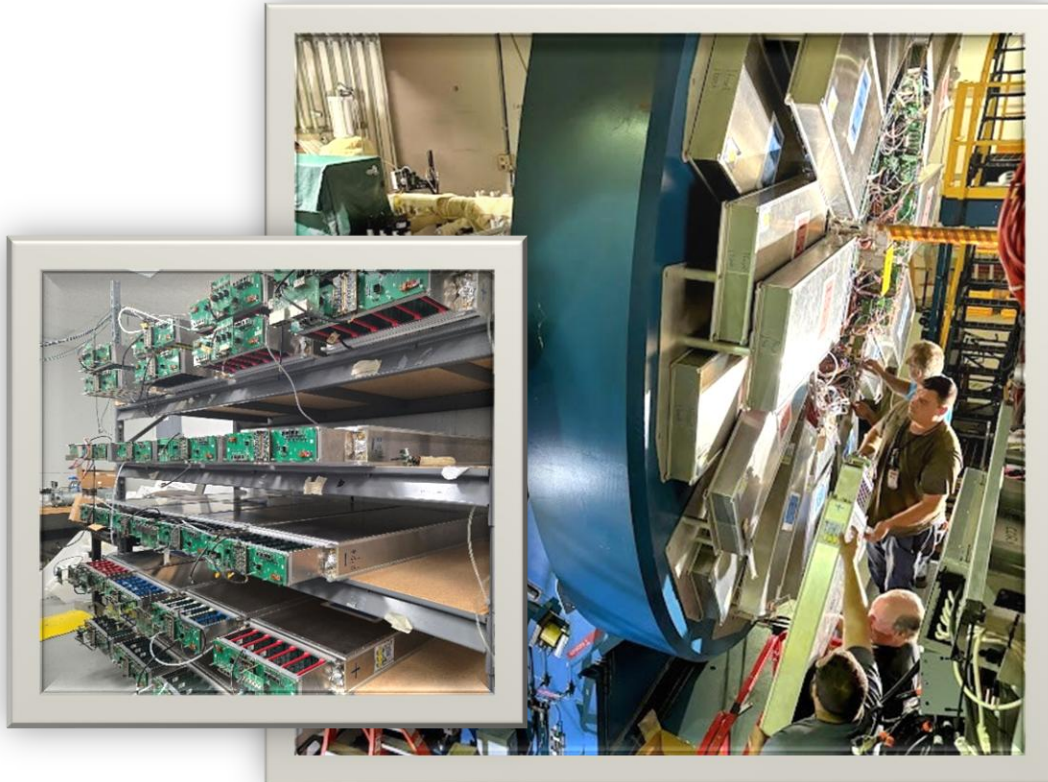

- Global interlock fault Tuesday, August 26, 5:30 am
- Water leak on West side (inside the pole-tip)
 - Move VPD; remove BBC; remove EPD
 - Open pole-tip; install scaffolding
 - Leak fixed on Wednesday morning; drying for two days
 - TPC FEE maintenance to follow
- Opened East pole-tip on Wednesday
 - Removal of all 36 ETOF modules for repair
 - Opportunistic TPC FEE maintenance in East
- Boards for ETOF repair shipped from GSI on Thursday
 - Experts will come for repair for potential fixed target run
 - Temporary storage in clean room in AH
- Purged flammable gas on Friday
- MCW shut off earlier than expected
 - Need TPC FEEs off before

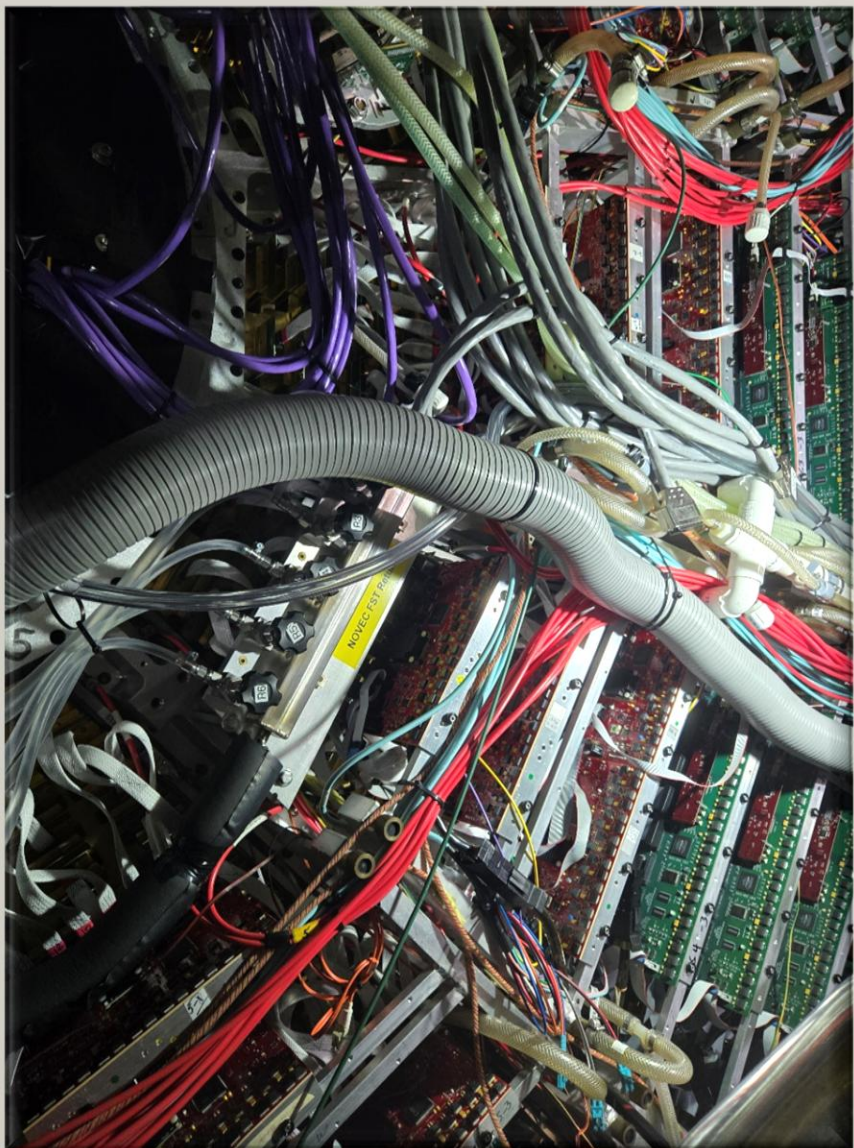

- Started switching electronics back on Saturday 9 am
- Gas watch shifts since Monday morning
 - Blue sheet complete today
- TPC maintenance today and tomorrow (West / East)
- Start closing up tomorrow (West)
 - Remove scaffolding
 - Reconnect cooling, electronics
- Re-installation of EPD late Thursday, then BBC & VPD
- Final check-out on Friday with magnet
