EIC - Working File

Data Date: 02-Jan-20

EIC - Activities with Gantt

TASK filter: WBS Path 06.10.04.04.01.

WBS Path	Activity ID	Activity Name	Original Duration	Start	Finish	Predecessors	Successors
Project: ECE06 EIC - Working File			1376	03-Oct-22	06-Apr-28		
WBS: ECE06.10 EIC Detector			1376	03-Oct-22	06-Apr-28		
WBS: ECE06.10.04 Particle Identification (PID)			1376	03-Oct-22	06-Apr-28		
WBS: ECE06.10.04.04 Time of Flight Detector (TOF)			1376	03-Oct-22	06-Apr-28		
WBS: ECE06.10.04.04.01 Central Timing and Tracking Layer Detector (CTTL)			1376	03-Oct-22	06-Apr-28		
10.04.04.01	E1004_41000	Final Design (CTTL)	523	03-Oct-22	04-Nov-24	L2_0180, L3_6010, EIPTOF _L_FY22	E1004_41010
10.04.04.01	E1004_41010	FDR - Final Design Complete - (CTTL)	0		04-Nov-24	E1004_41000	E1004_41020, PM_0101_5100
10.04.04.01	E1004_41020	Prepare Specs & SOWs for All Procurements & Fabs (CTTL)	110	30-May-24	04-Nov-24	E1004_41010	E1004_41040, E1004_41030
10.04.04.01	E1004_41030	APP/Acquisition Plan Approval (CTTL)	20	05-Nov-24	05-Dec-24	E1004_41020	E1004_41040
10.04.04.01	E1004_41040	Pin Requisition (CTTL)	0		05-Dec-24	E1004_41020, E1004_41030	E1004_41050
10.04.04.01	E1004_41050	Procurement Process (CTTL)	172	06-Dec-24	12-Aug-25	E1004_41040	E1004_41060
10.04.04.01	E1004_41060	Contract Award (CTTL)	1	13-Aug-25	13-Aug-25	E1004_41050	E1004_41070
10.04.04.01	E1004_41070	First Article (CTTL)	207	14-Aug-25	12-Jun-26	E1004_41060	E1004_41090, E1004_41080, E1004_41120
10.04.04.01	E1004_41080	First Article In-Kind (CTTL)	207	14-Aug-25	12-Jun-26	E1004_41070	E1004_41090, E1004_41120
10.04.04.01	E1004_41090	Construction - Labor (CTTL)	600	14-Aug-25	11-Jan-28	E1004_41070, E1004_41080	E1004_41100, E1004_41120
10.04.04.01	E1004_41100	Construction - Materials (CTTL)	600	14-Aug-25	11-Jan-28	E1004_41090	E1004_41110, E1004_41120
10.04.04.01	E1004_41110	Construction - Materials In-Kind (CTTL)	600	14-Aug-25	11-Jan-28	E1004_41100	E1004_41120
10.04.04.01	E1004_41120	Vendor Delivery (CTTL)	0		11-Jan-28	E1004_41070, E1004_41080, E1004_41090, E1004_41100, E1004_41110	E1004_41130
10.04.04.01	E1004_41130	Test, Final Acceptance (CTTL)	60	12-Jan-28	06-Apr-28	E1004_41120	E1004_41140
10.04.04.01	E1004_41140	Ready for Installation (CTTL)	0		06-Apr-28	E1004_41130	E0704_06015

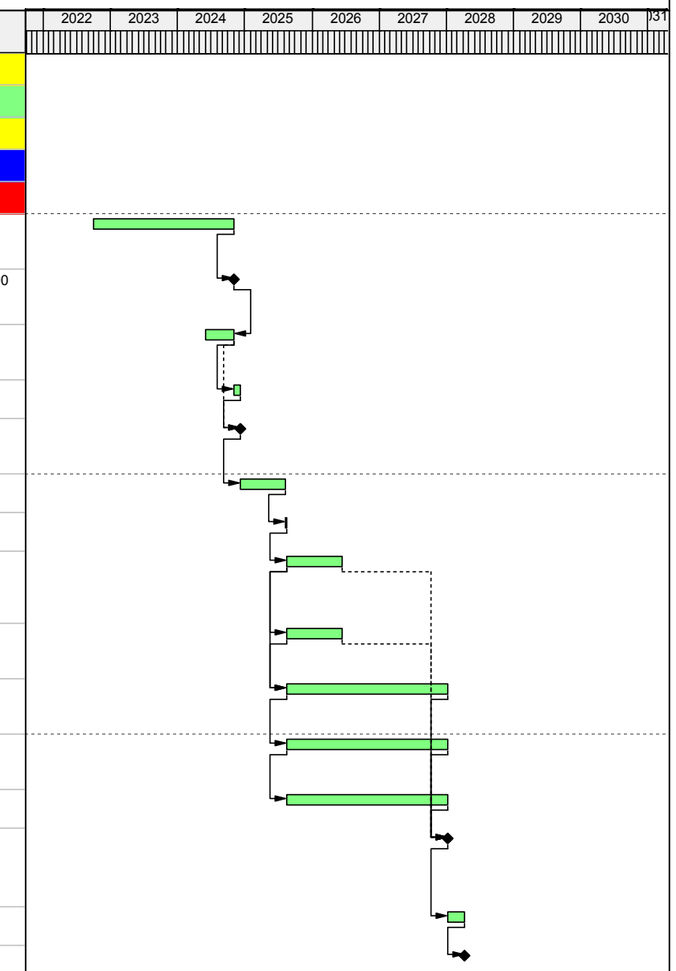

Remaining Level of Effort | Remaining Work | SVT | L3 Milestone
Actual Level of Effort | Critical Remaining Work | L1 Milestone
Actual Work | Milestone | L2 Milestone

Prepared by: ewoolsey | Date: 14-Jun-23 I Time: 15:30
